



MEMO

TO	Katie Daugherty, ODEQ
FROM	Brendan Robinson, PE, ERM; Todd Slater, LSS
DATE	17 February 2025
REFERENCE	0732445.204
SUBJECT	Groundwater Source Control Measure Monthly Performance Monitoring Report

1. INTRODUCTION

The Oregon Department of Environmental Quality (ODEQ), in its letter dated 31 May 2019 and in the subsequent meeting with Legacy Site Services LLC (LSS) and Environmental Resources Management, Inc. (ERM) on 2 July 2019, requested that LSS initiate monthly status reports associated with the onsite groundwater source control measure (GW SCM) at the Arkema site (Site) consistent with the Performance Monitoring Plan (PMP; ERM 2014¹) beginning July 2019. The Site is located at 6400 NW Front Avenue in Portland, Oregon, and the Site location is shown on Figure 1. The 2014 PMP was prepared pursuant to the Order on Consent issued by ODEQ, signed on 31 October 2008 (ODEQ No. LQVC-NWR-08-04; Consent Order). The purpose of the PMP was to present the monitoring, reporting, and adaptive management processes used during implementation of the GW SCM. On 30 November 2021, ODEQ directed LSS that following the October 2021 Monthly Performance Monitoring Report (MPR), subsequent MPRs would be suspended pending the implementation of the Groundwater Extraction Enhancement (GEE) project in 2022. During that time, ODEQ requested monthly schedule updates in lieu of MPRs. The trench wells installed as part of the GEE project were started on 27 November 2022, and MPR writing restarted in December 2022. The purpose of the GEE project was to install new extraction capacity to achieve the Capture Zone Objectives.

On 6 June 2024, ODEQ requested that LSS and ERM reduce the scope of future MPRs to facilitate faster review. On 11 September 2024, ODEQ agreed for the first amended MPR to be the August 2024 MPR submitted in October 2024.

2. GWET SYSTEM PERFORMANCE

The GWET system maintained 100 percent uptime during the month of December 2024. Consequently, the average system influent flow rate was 30.95 gallons per minute (gpm) for the

¹ ERM-West, Inc. 2014. *Revised Final Performance Monitoring Plan – Groundwater Source Control Measure, Arkema Inc. Facility, Portland, Oregon*. July 2014.

entire month of December 2024, including non-operational periods and the average operational influent flow during operational periods was also 30.95 gpm.

Extraction wells, pumps, and conveyance lines become fouled with accumulated solids over time. A proactive pump removal and maintenance program is in place to address pump fouling. Regularly scheduled redevelopment is anticipated to maintain the productivity of the groundwater extraction trenches and recovery wells. Conveyance line cleaning will be conducted as needed based on analysis of backpressure.

Compared to November 2024, the December 2024 average system influent flow rate was 3.41 gpm greater. During this same time period, the average Shallow Zone groundwater elevation increased by 0.61 feet, and the average Intermediate Zone groundwater elevation increased by 0.87 feet, as shown on Attachments A-1 and A-2. The increase in average monthly groundwater extraction rate in December 2024 compared to November 2024 is likely a result of the seasonal increase in river elevation, and the resulting increase in the groundwater elevation.

River elevations are shown over time on Attachments A-1 and A-2, and in an inset on the potentiometric surface maps (Figures 2 through 4). The river elevation has generally been trending downward since January 2024. The river elevation had an increase December 2024 had an average elevation of 9.99 feet North American Vertical Datum of 1988 (NAVD88) with a minimum elevation of 6.44 feet NAVD88 and a maximum elevation of 14.67 feet NAVD88. The river elevation had an increase of 0.70 feet NAVD88 compared to November 2024.

LSS is continuing to optimize extraction rates within the system to increase flow rates at each operational well until either the extraction rates specified in the *Groundwater Extraction Enhancement Final Design Report* (ERM 2022²) are achieved, the wells are producing the maximum quantity of water possible, or until the Capture Zone Objectives are met.

Actions taken in December 2024 to optimize flow rates included:

- Procuring and testing a smaller Hydropuls device to focus redevelopment of the horizontal well screens in the extraction wells. Redevelopment of the horizontal screen section is scheduled for January 2025.
- The smaller Hydropuls tool was optimized with new hose connections and fittings to reduce the overall length of the rigid section of the tool to help it navigate the sweeping 45-degree elbows in the extraction trenches. Test results demonstrate that the smaller Hydropuls tool with the optimized fittings will be able to enter and exit the horizontal screens of the extraction trenches.

2.1 GWET PLANT OPERATIONS

The groundwater extraction and treatment (GWET) plant operated within permit conditions during the reporting period. There were no shutdowns during December 2024.

² ERM-West, Inc. 2022. *Final Design Report, Arkema Inc. Facility, Portland, Oregon*. May 2022.

3. CAPTURE ZONE EVALUATION

As described in the PMP, the purpose of hydraulic monitoring (i.e., groundwater elevation data) is to provide sufficient data to demonstrate an inward hydraulic gradient across the groundwater barrier wall (GWBW) and to evaluate the effective hydraulic capture produced by the GW SCM.

3.1 GROUNDWATER ELEVATION MONITORING

Groundwater elevation monitoring was completed on 6 December 2024. The Serfes (1991)³ method was used to account for tidal variations of groundwater and river elevations as described in the PMP. Horizontal and vertical gradients were calculated and plotted over time as shown in Attachments B-1 and B-2. Groundwater elevations, horizontal gradients, and vertical gradients from 6 December 2024 are tabulated in Attachment B-3 and Attachment B-4.

3.2 POTENTIOMETRIC SURFACE, GROUNDWATER ELEVATION DIFFERENCE MAPS, AND GROUNDWATER FLOW DIRECTIONS

Groundwater elevation data collected on 6 December 2024 was used to prepare potentiometric surface maps based on manual measurements and averaged transducer groundwater elevations (Figures 2 through 4) and vertical gradient difference maps (Figures 5 and 6).

The generalized flow direction indicated by the potentiometric surface maps shows groundwater flow from upgradient toward the GBW. Potentiometric surface maps (Figures 2, 3, and 4) show generalized groundwater movement to the extraction trenches in the Shallow, Intermediate, and Deep Zones due to GW SCM pumping, and cones of depression are apparent around the groundwater extraction trenches in the Shallow and Intermediate Zones. Horizontal gradient at gradient control cluster 2 (GCC 2) was inward in December 2024, nearly zero at GCC 1 and decreasingly outward at GCC 3, GCC 4 and GCC 5, as shown in Attachments B-1 and B-3.

Vertical gradients were calculated for each vertical well pair and are plotted on Figures 5 and 6. Vertical groundwater gradients and trend lines are shown in Attachments B-2 and B-4. Vertical groundwater gradients exterior to the GBW were neutral to slightly downward between the Shallow and Intermediate Zones and between the Intermediate and Deep Zones.

Vertical gradients interior to the GBW between the Shallow Zone and Intermediate Zone were inward at GCC 2, nearly neutral at GCC 3 and GCC 5, and downward at GCC 6, GCC 4, and GCC 1. Note that the vertical gradient for GCC 1 is exaggerated as a result of the localized pressure zone where soils are tight and water is relatively immobile. Vertical gradients interior to the GBW between the Intermediate Zone and Deep Zone were upward at GCC 6, nearly neutral at GCC 2 and GCC 4, and downward at GCC3 and GCC 5. Vertical gradient could not be calculated for GCC 1 because of a transducer failure.

³ Serfes, Michael. 1991. "Determining the Mean Hydraulic Gradient of Ground Water Affected by Tidal Fluctuations." *Groundwater* 29(4): July–August.

4. CONCLUSIONS

Analysis of horizontal gradients over time indicate that the extraction wells are performing better than the historical recovery wells, and horizontal gradients are periodically inward, and the magnitude of outward gradients are decreasing over time, as shown on Attachment B-1. The extraction rates throughout the GWET system will continue to be optimized to meet Target Capture Objectives. Redevelopment of the trenches is planned to mitigate accumulation of silt in the filter pack in both the vertical and horizontal sections using impulse redevelopment techniques, and resonant technology. These efforts will be targeted at trenches that are currently underperforming, including Trenches 1, 4, 5, and 6. LSS will continue to optimize new extraction wells, including pump maintenance and upgrades. Additional modifications to the system, if needed to progress toward capture objectives, will be included in subsequent MPRs. The project schedule provided as Attachment C summarizes planned activities.

Attachment D shows the average influent groundwater flow rate from April 2019 through December 2024. As shown on this figure, the extraction trenches are removing approximately three times more water than the legacy system and achieving lower horizontal gradients over time.

Regards,



Brendan Robinson, PE
Partner

ATTACHMENTS

FIGURE 1 – SITE LAYOUT

FIGURE 2 – SHALLOW ZONE GROUNDWATER CONTOURS

FIGURE 3 – INTERMEDIATE ZONE GROUNDWATER CONTOURS

FIGURE 4 – DEEP ZONE GROUNDWATER CONTOURS

FIGURE 5 – SHALLOW TO INTERMEDIATE ZONE VERTICAL HEAD DIFFERENCE MAPS

FIGURE 6 – INTERMEDIATE TO DEEP ZONE VERTICAL HEAD DIFFERENCE MAPS

ATTACHMENT A-1 – OPERATIONAL PUMPING RATE GRAPH

ATTACHMENT A-2 – AVERAGE MONTHLY PUMPING RATE GRAPH

ATTACHMENT A-3 – GWET SYSTEM GROUNDWATER EXTRACTION RATES TABLE

ATTACHMENT B-1 – HORIZONTAL GRADIENTS SUMMARY GRAPH

ATTACHMENT B-2 – VERTICAL GRADIENTS SUMMARY GRAPH



ATTACHMENT B-3 – WATER LEVELS AND HORIZONTAL GRADIENTS TABLE

ATTACHMENT B-4 – WATER LEVELS AND VERTICAL GRADIENTS TABLE

ATTACHMENT C – PROJECT SCHEDULE

ATTACHMENT D – AVERAGE GROUNDWATER EXTRACTION RATE GRAPH

DRAWN BY: Jake Sullivan
REVISED: 02/06/2023. SCALE: 1:1,440 when printed at 11x17
M:\US\Projects\S-U\Total\Arkema Portland\Groundwater Source Control\maps\MP\GWET PMP 202212\Figure 1 Site Layout for MPR .mxd

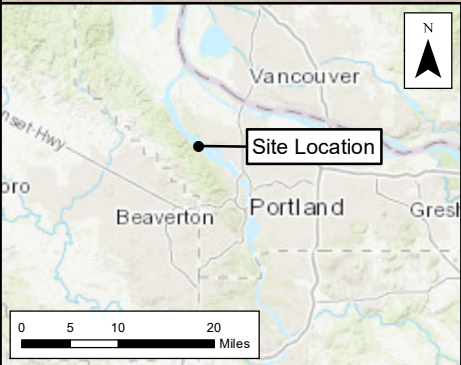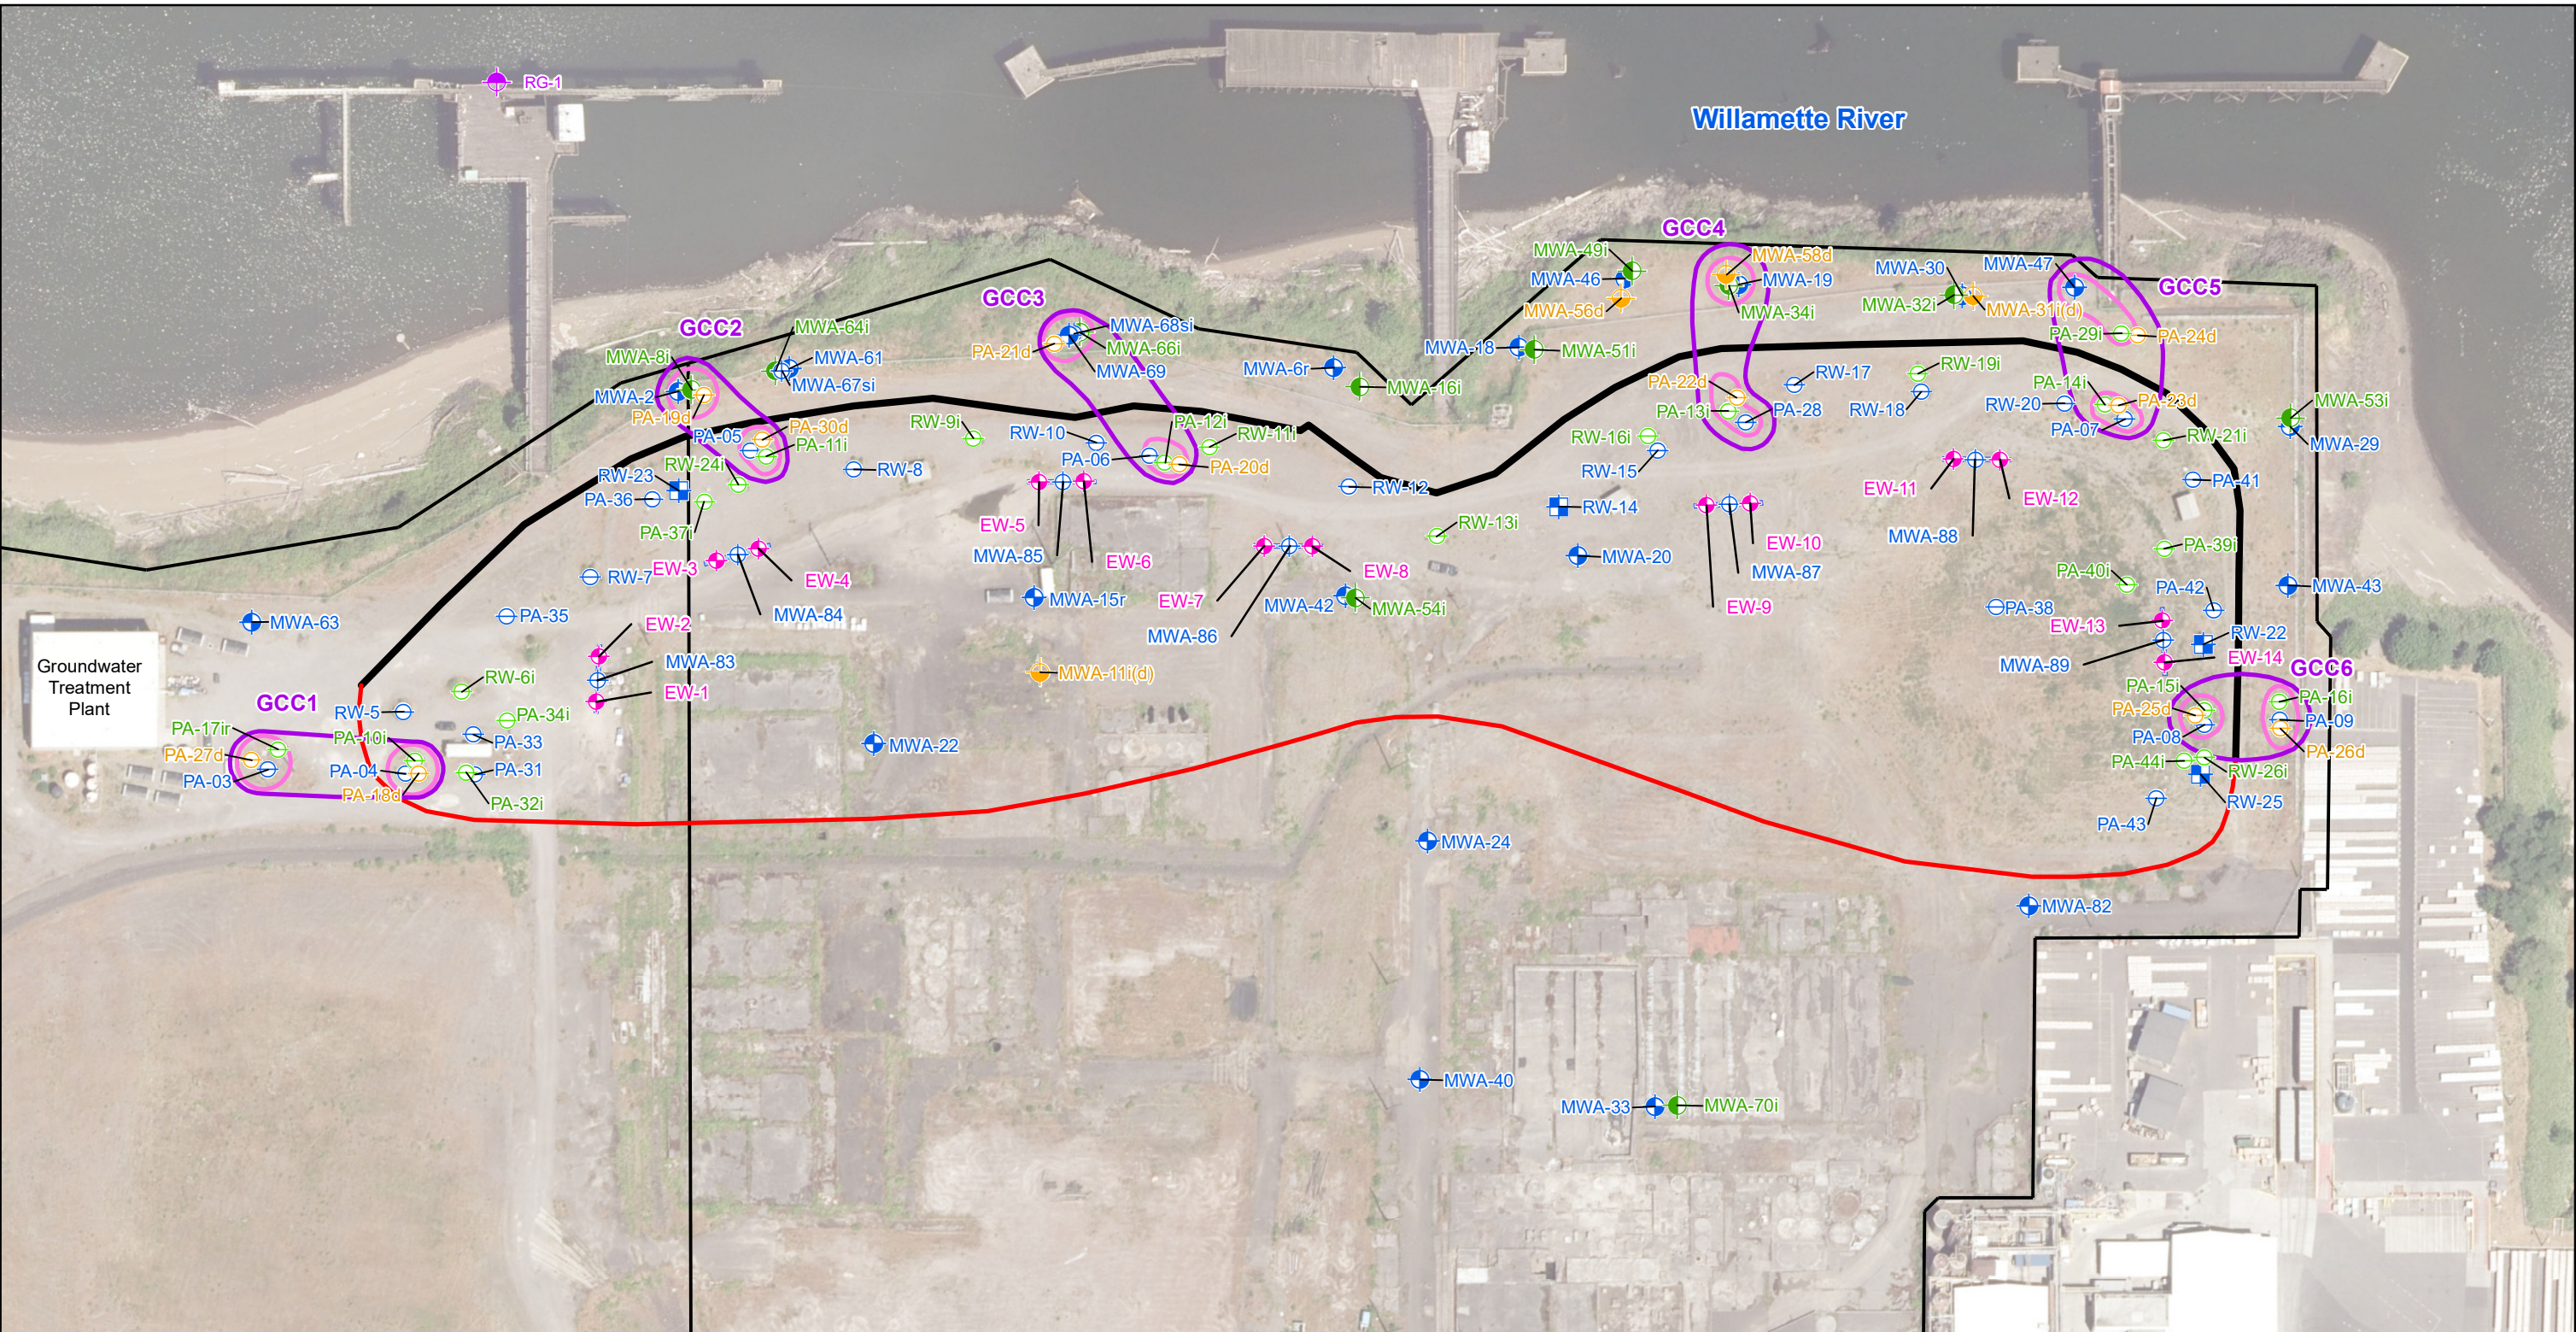

Legend

- Shallow Zone Monitoring Well
- Intermediate Zone Monitoring Well
- Shallow-Intermediate Zone Monitoring Well
- Deep Zone Monitoring Well
- Shallow Zone Piezometer
- Intermediate Zone Piezometer
- Deep Zone Piezometer
- Shallow Zone Recovery Well
- River Gauge
- Trench Extraction Well
- Target Capture Zone
- Barrier Wall Alignment
- Parcel and Property Boundaries

GradientClusters

Type

- Gradient Control Cluster
- Vertical Flow Cluster
- Extraction Trench

Figure 1

Site Layout

Monthly Progress Report


Groundwater Source Control Measure

Arkema Inc.



Portland, Oregon

Environmental Resources Management
www.erm.com

Source: City of Portland Aerial Imagery, flown Summer 2021; NAD 1983 StatePlane Oregon North FIPS 3601 Feet Intl

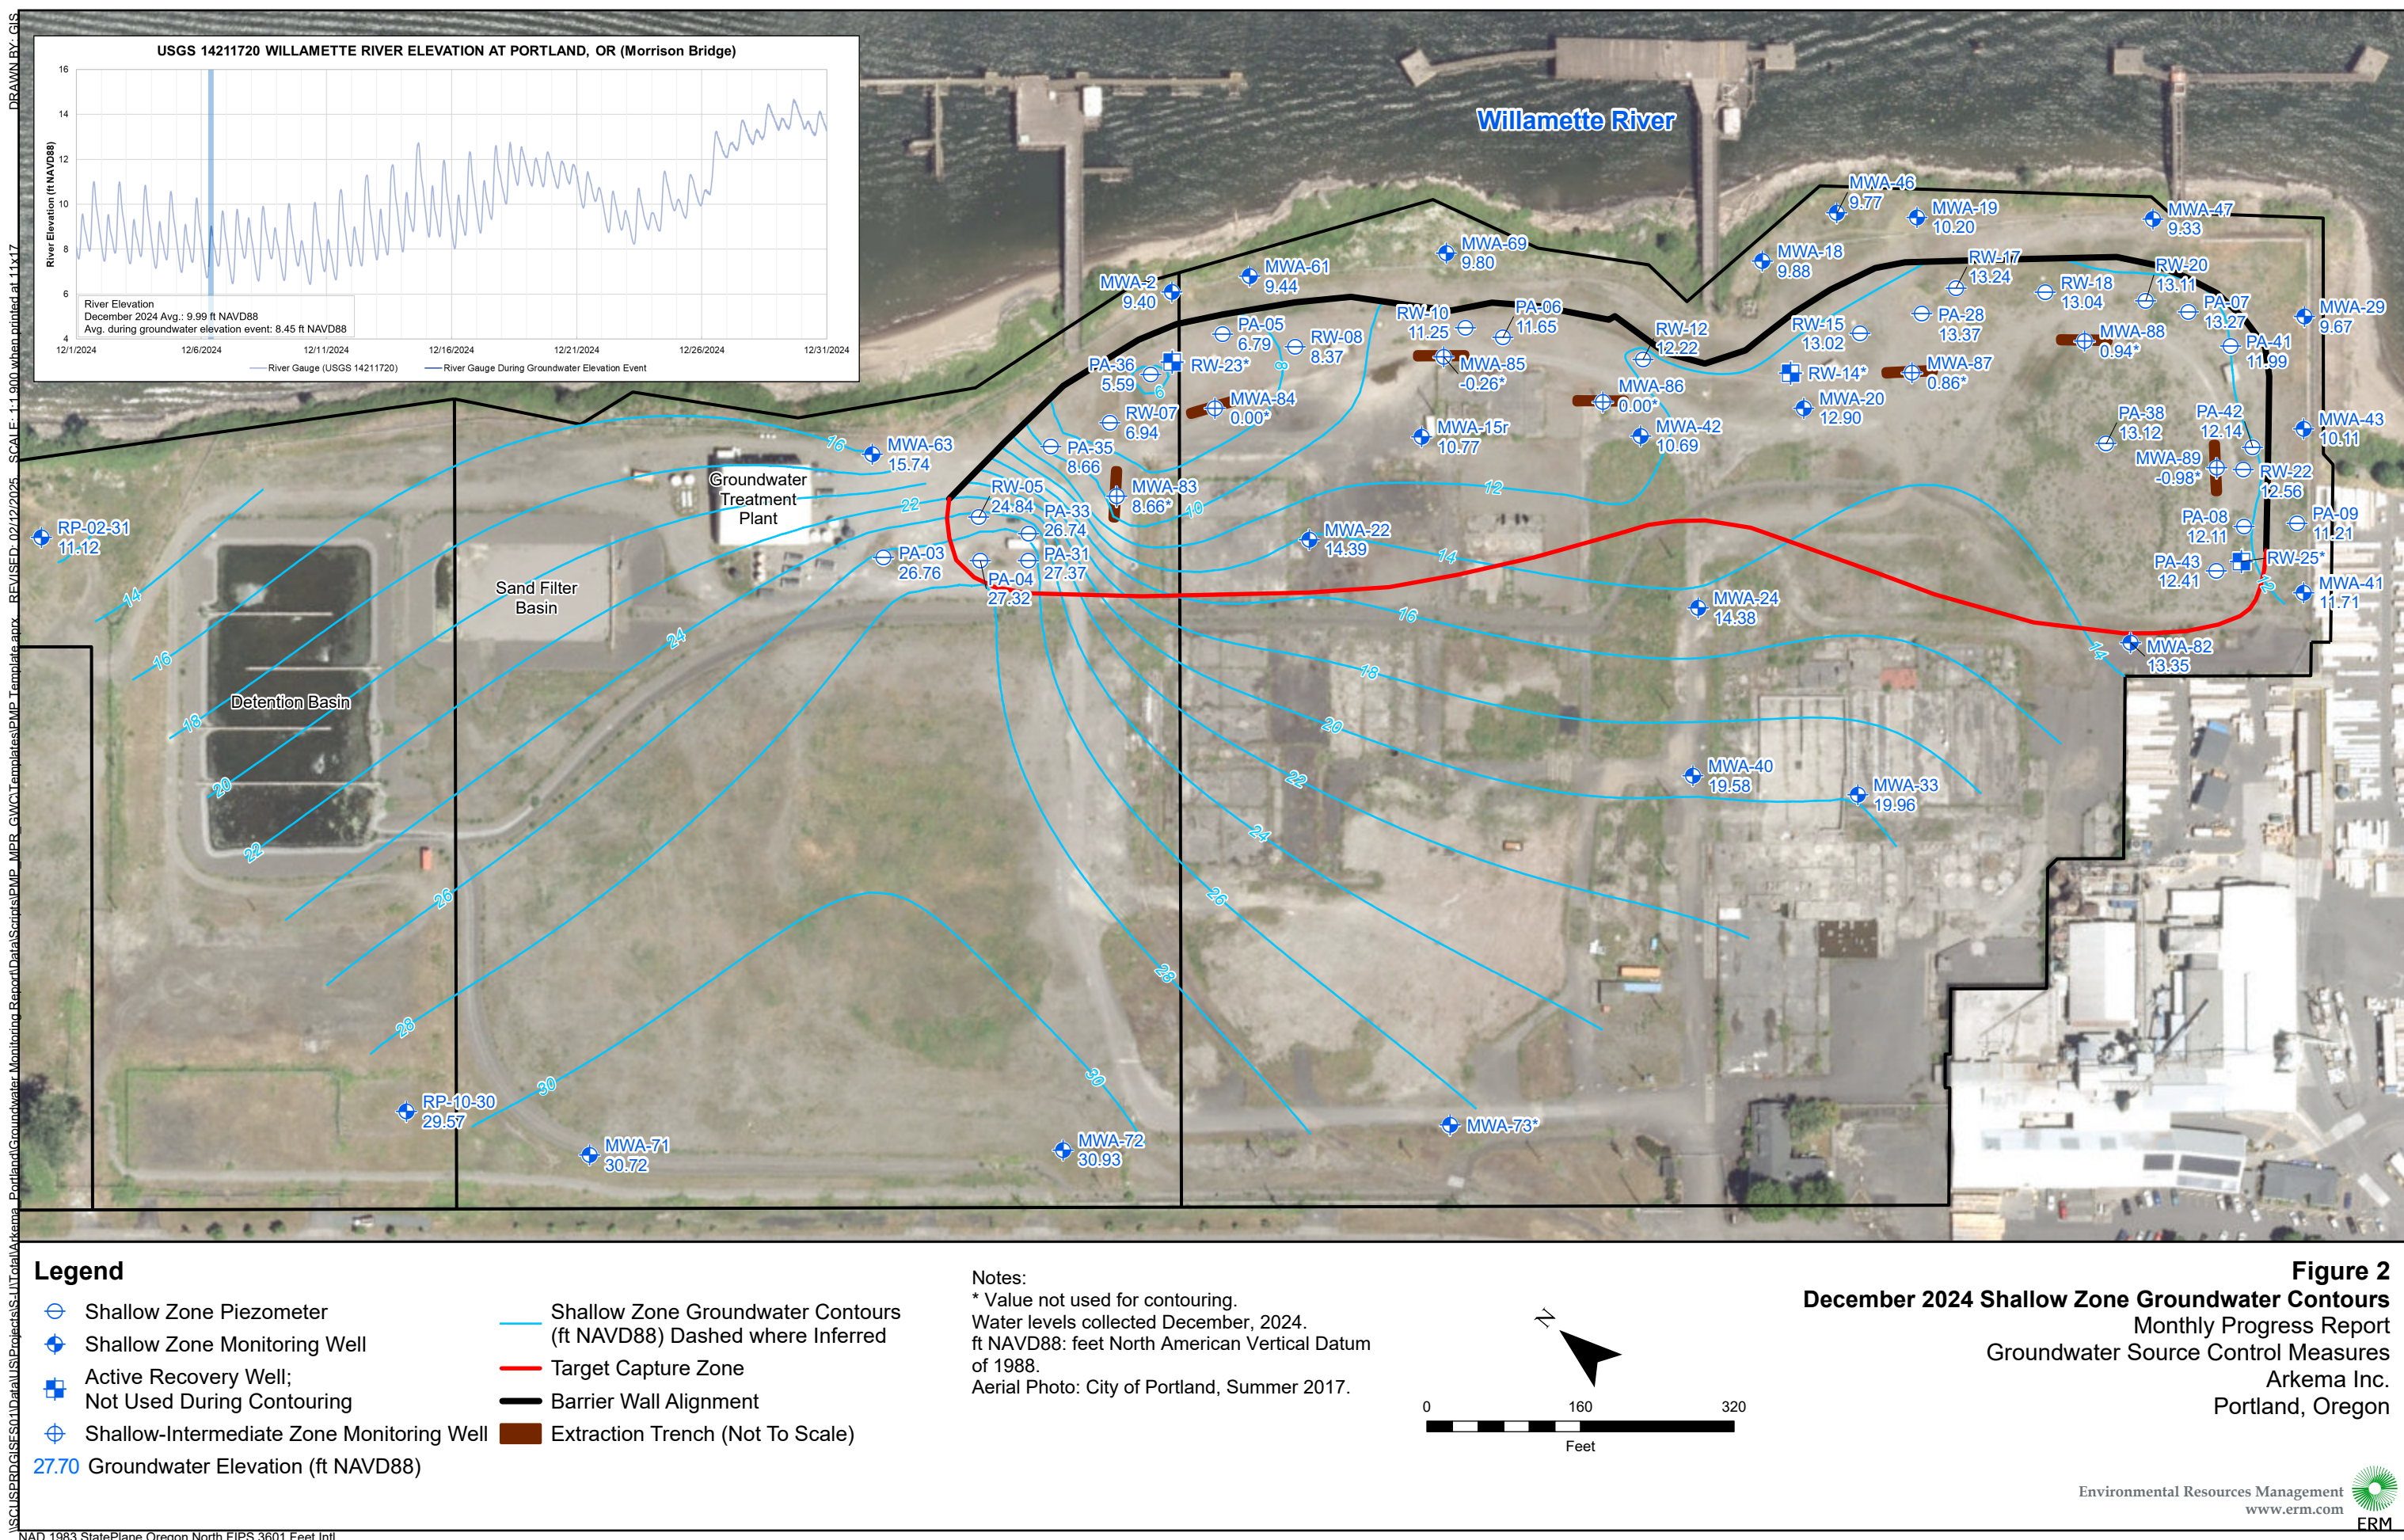

\\SC\USPBD\GIS\ES\01\Data\US\Projects\SL\Total\Arkema_Portland\Groundwater_Monitoring\Report\Data\Scripts\PMMP_MPR_GWCTemplates\PMMP_Template.aprx REVISED: 02/12/2025 SCALE: 1"=800' when printed at 11x17 DRAWN BY: GIS

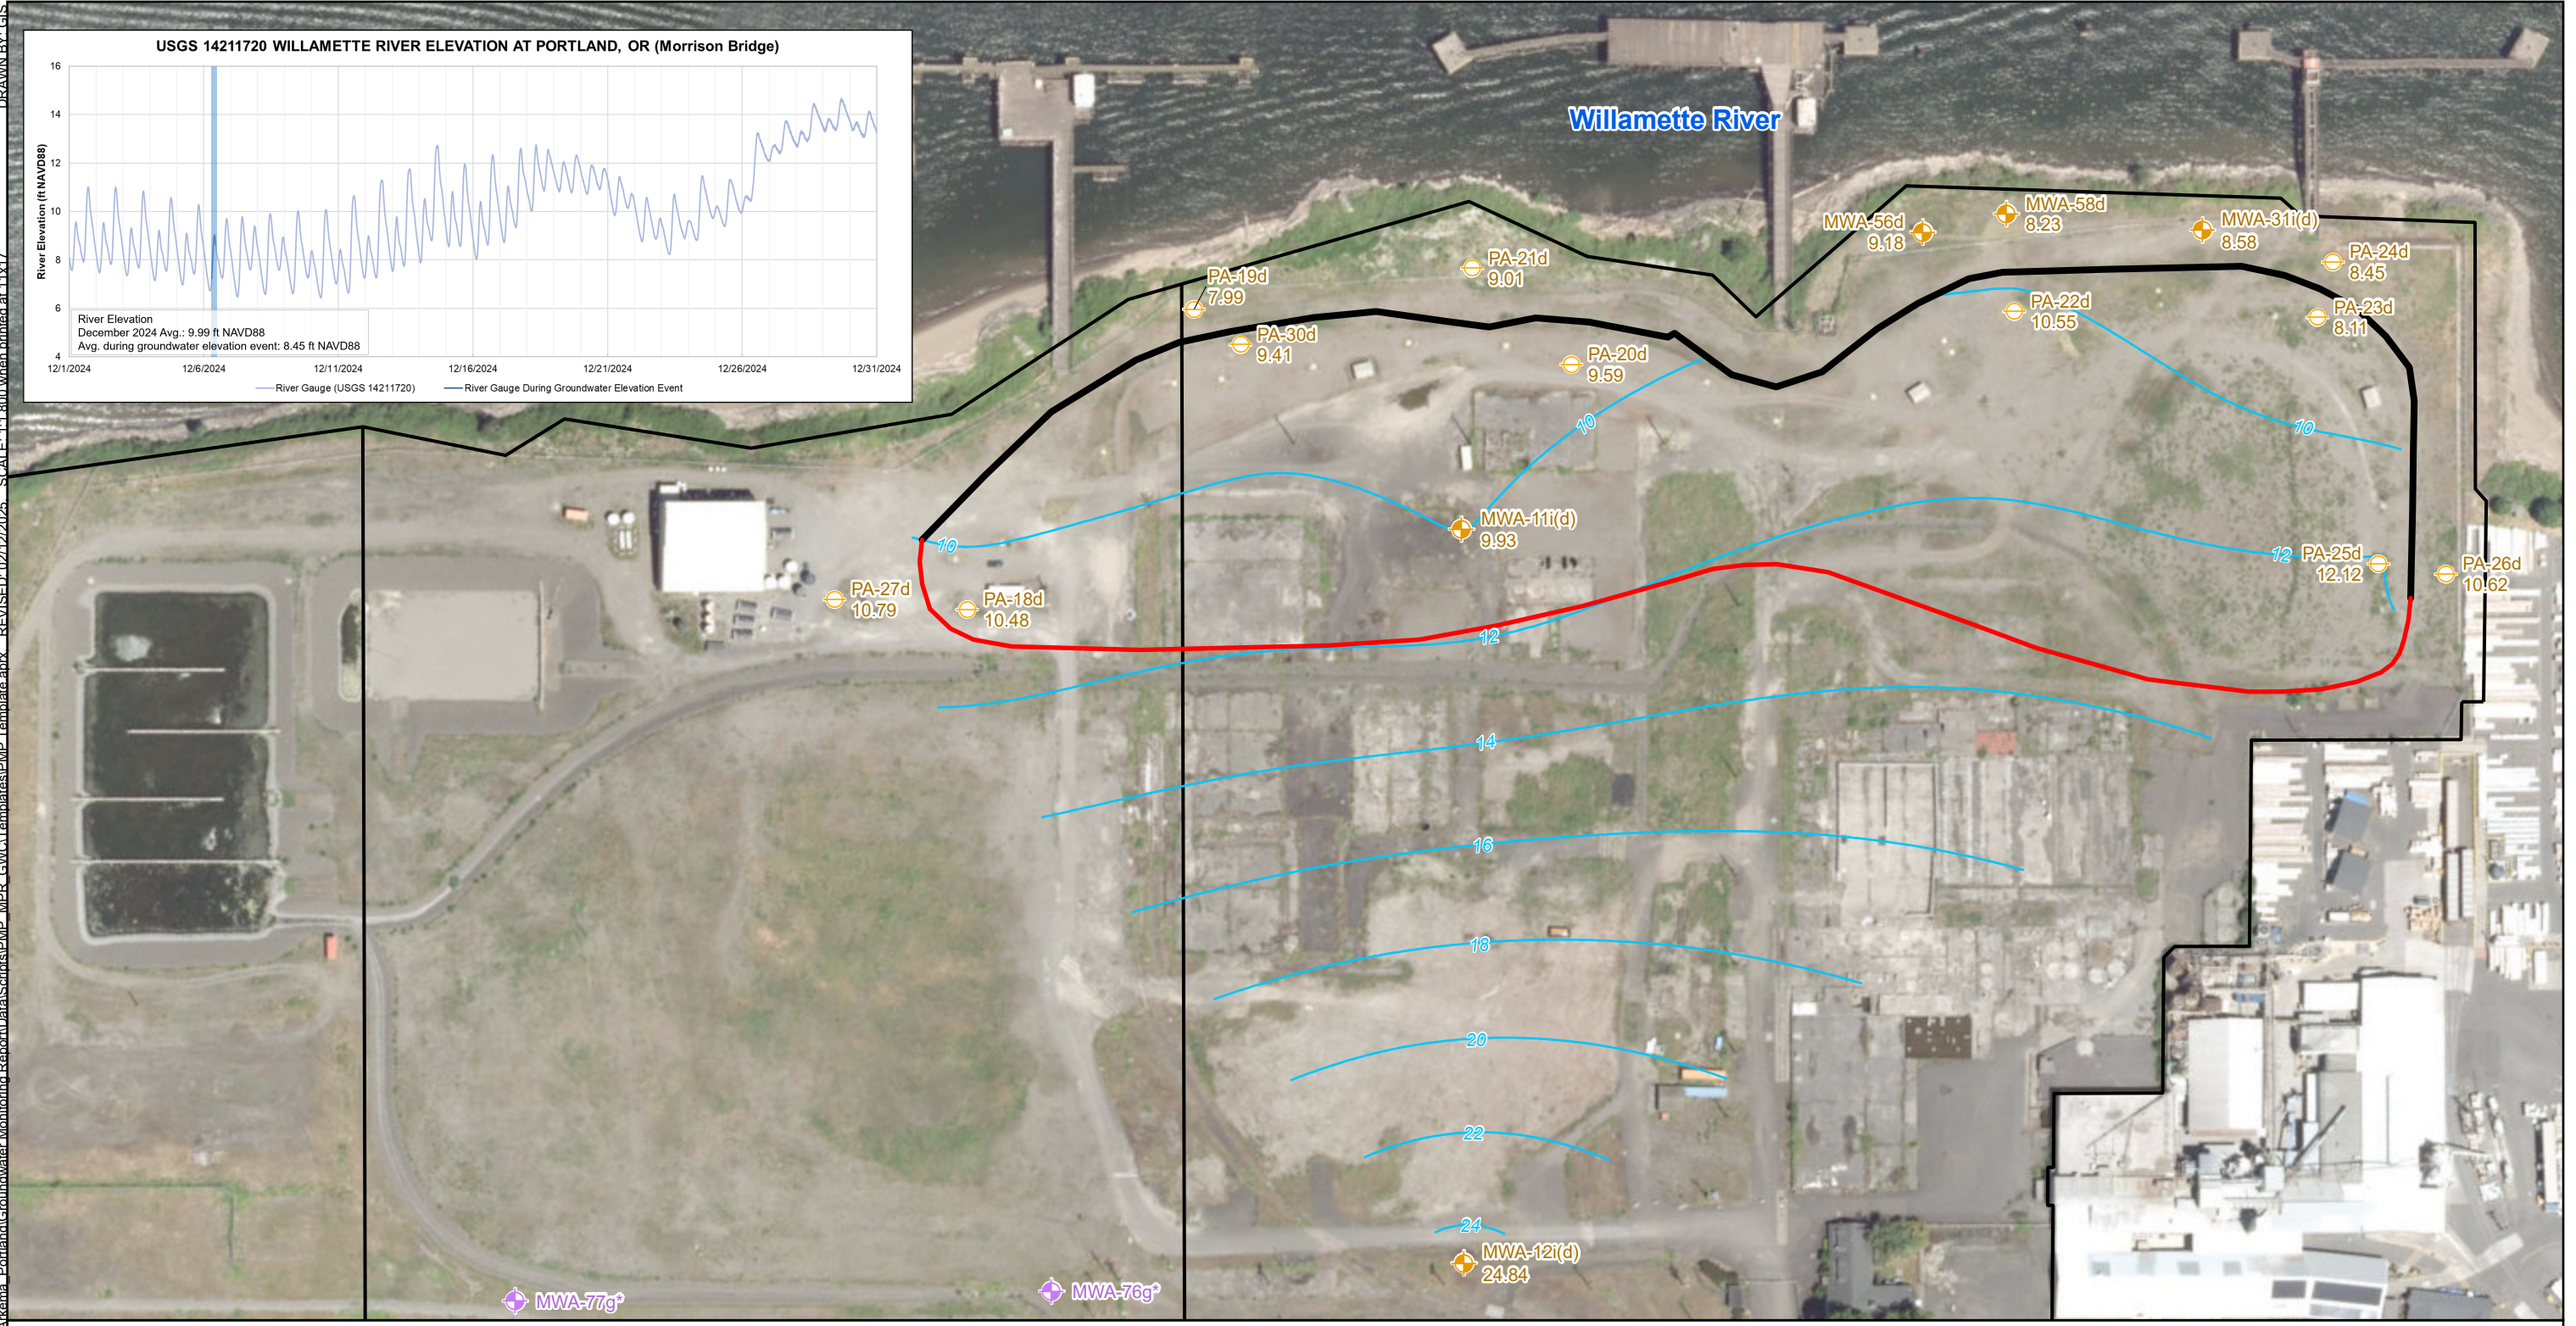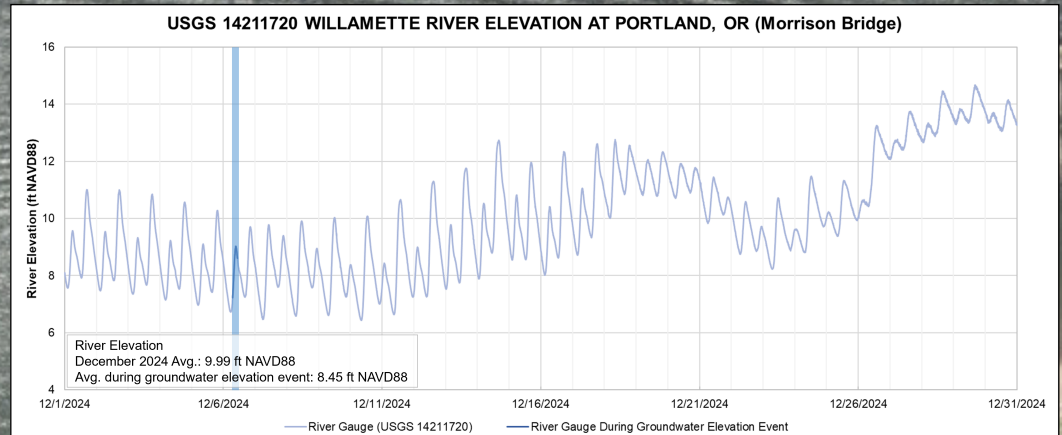

Legend

- Deep Zone Piezometer
- ◆ Deep Zone Monitoring Well
- ◆ Gravel Zone Monitoring Well
- 27.70 Groundwater Elevation (ft NAVD88)
- Deep Zone Groundwater Contours (ft NAVD88)
Dashed where Inferred
- Target Capture Zone
- Barrier Wall Alignment

Notes:
* Value not used for contouring.
Gravel zone wells not used in contouring.
Water levels collected December, 2024.
ft NAVD88: feet North American Vertical Datum of 1988.
Aerial Photo: City of Portland, Summer 2017.




Figure 4
December 2024 Deep Zone Groundwater Contours
Monthly Performance Report
Groundwater Source Control Measures
Arkema Inc.
Portland, Oregon

\\SC\USPRD\GIS\ES\01\Data\US\Projects\SL\UTotal\Arkema_Portland\Groundwater_Monitoring_Report\Data\Scripts\MPR_GWC\Templates\MPM_Template.aprx REVISED: 02/12/2025 SCALE: 1"=560 when printed at 11x17 DRAWN BY: GIS



Legend

	Shallow Zone Monitoring Well		Active Recovery Well		Downward Gradient
	Intermediate Zone Monitoring Well		Trench Extraction Well		Upward Gradient
	Shallow Zone Piezometer		Target Capture Zone		
	Intermediate Zone Piezometer		Barrier Wall Alignment		
	Shallow Zone Recovery Well		Extraction Trench		
	Trench Extraction Well		Gradient Control Cluster		
			Vertical Flow Cluster		

Notes:

Brown gradient: Downward gradient.
Green gradient: Upward gradient.
Vertical gradient calculated as shallow zone minus intermediate zone potentiometric surfaces.
Water levels collected December, 2024.
Aerial Photo: City of Portland, Summer 2017.

0 130 260
Feet

Figure 5

December 2024 Shallow to Intermediate Zone Vertical Head Difference
Monthly Progress Report
Groundwater Source Control Measures
Arkema Inc.
Portland, Oregon

Environmental Resources Management
www.erm.com
ERM




ATTACHMENT A-1

OPERATIONAL PUMPING RATE GRAPH

Attachment A-1

Operational Pumping Rate Graph
Arkema Inc. Facility
Portland, Oregon

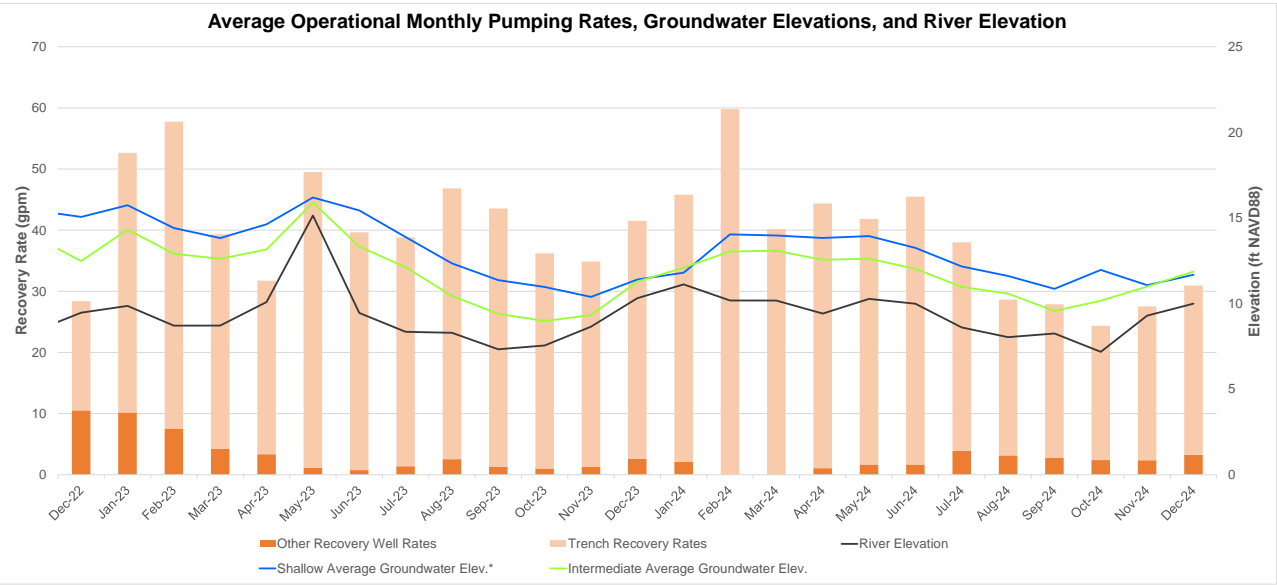




ATTACHMENT A-2

AVERAGE MONTHLY PUMPING RATE
GRAPH

Attachment A-2

Average Pumping Rate Graph Arkema Inc. Facility Portland, Oregon

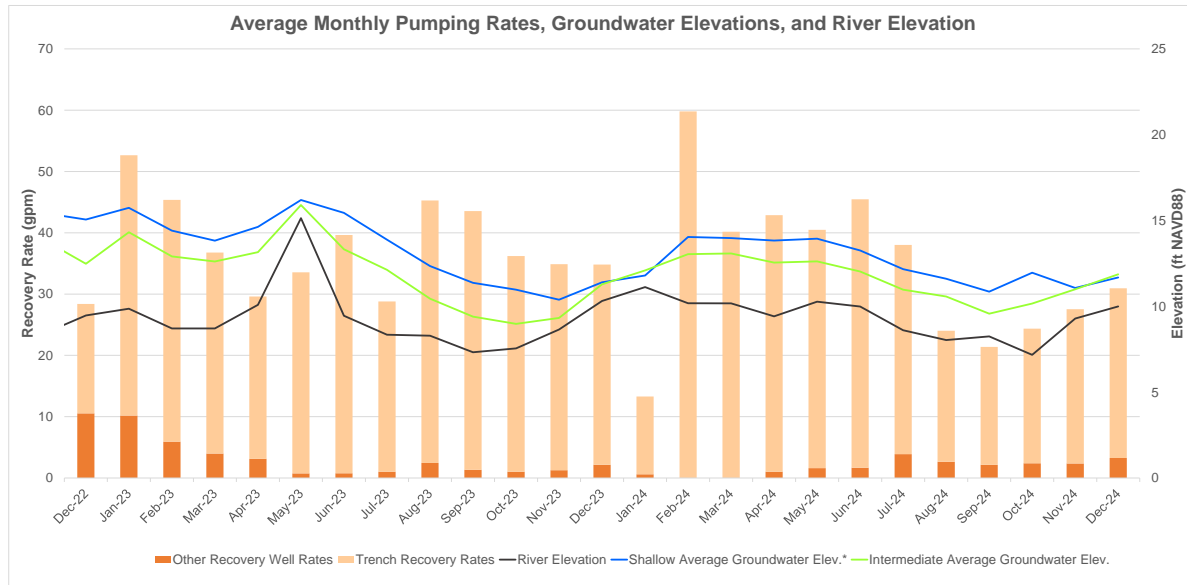



ATTACHMENT A-3

GWET SYSTEM GROUNDWATER
EXTRACTION RATES TABLE

Attachment A-3

GWET System Groundwater Extraction Rates Table Arkema Inc. Facility Portland, Oregon

Recovery Well	December 2024 Average Operational Pumping Rate (gpm)	December 2024 Average Monthly Pumping Rate (gpm)
RW-14	0.95	0.95
RW-22*	0.00	0.00
RW-23	0.91	0.91
RW-25	1.39	1.39
EW-01	1.04	1.04
EW-02*	0.00	0.00
EW-03	9.93	9.93
EW-04	0.21	0.21
EW-05*	3.79	3.79
EW-06	2.11	2.11
EW-07*	0.00	0.00
EW-08	1.74	1.74
EW-09	1.68	1.68
EW-10*	0.00	0.00
EW-11	0.83	0.83
EW-12	1.24	1.24
EW-13	5.05	5.05
EW-14	0.07	0.07
Total	30.95	30.95

* = Recovery well not in service during reporting period

gpm = gallon per minute



ATTACHMENT B-1

HORIZONTAL GRADIENTS SUMMARY
GRAPH


Attachment B-1

Horizontal Gradients Summary: December 2024


Arkema Inc. Facility

Portland, Oregon


Horizontal Gradients - Shallow Zone

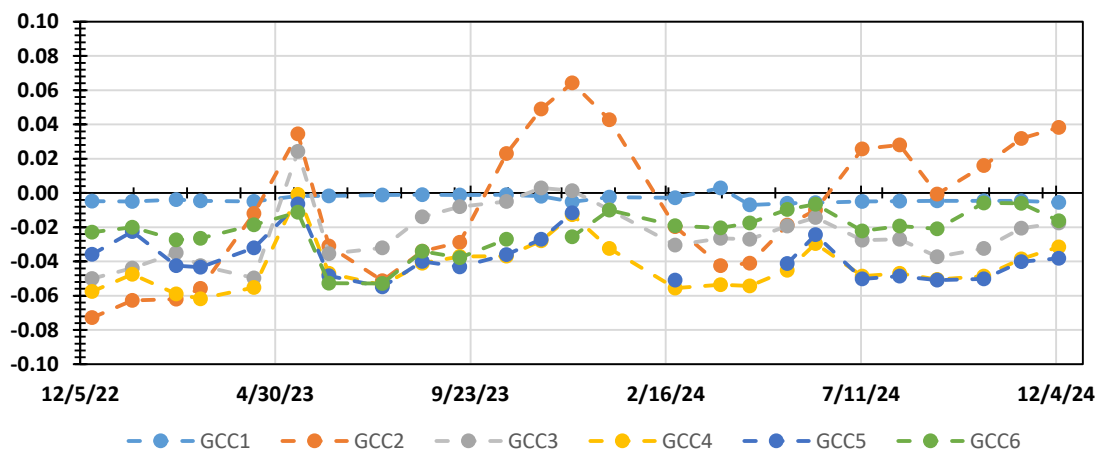

Horizontal Gradients - Intermediate Zone

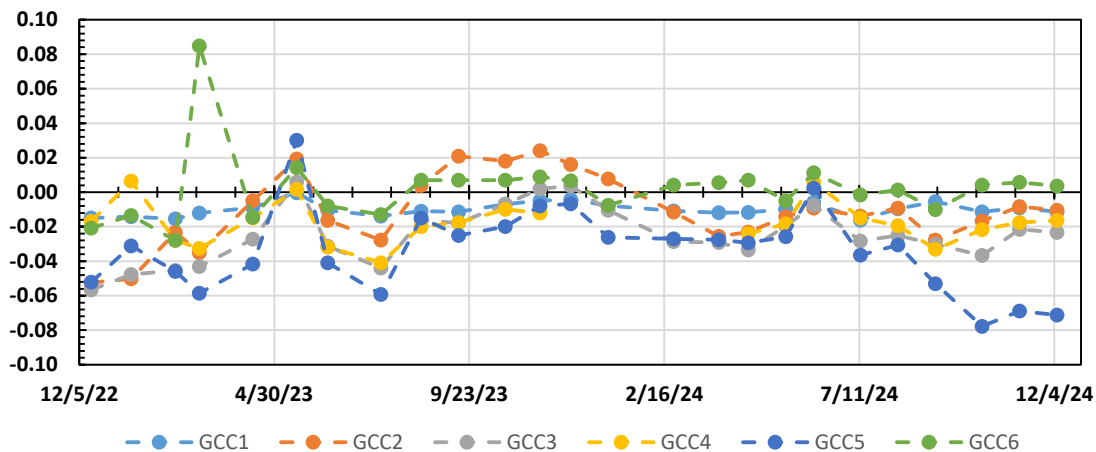

Horizontal Gradients - Deep Zone

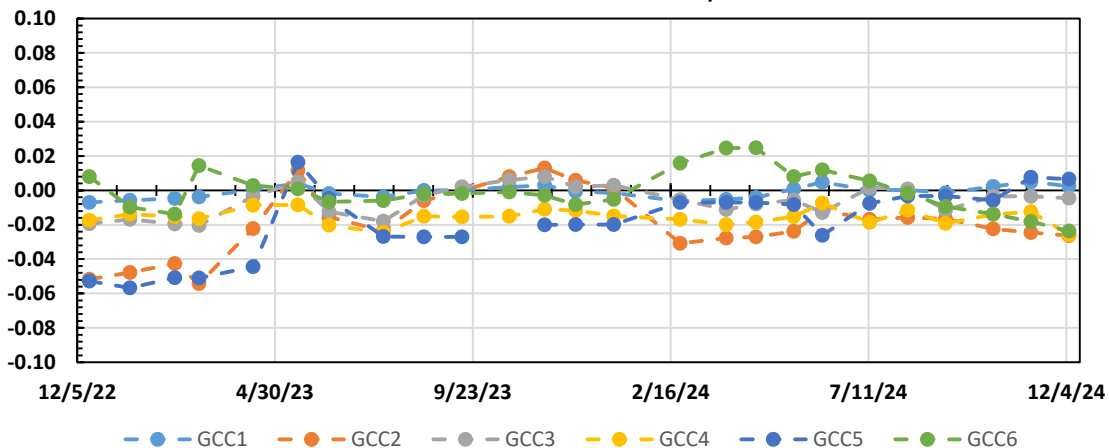

Positive horizontal gradient indicates an inward hydraulic gradient across the GWBW.



ATTACHMENT B-2

VERTICAL GRADIENTS SUMMARY
GRAPH


Attachment B-2

Vertical Gradients Summary: December 2024


Arkema Inc. Facility

Portland, Oregon


Vertical Gradients - Interior SZ-IZ

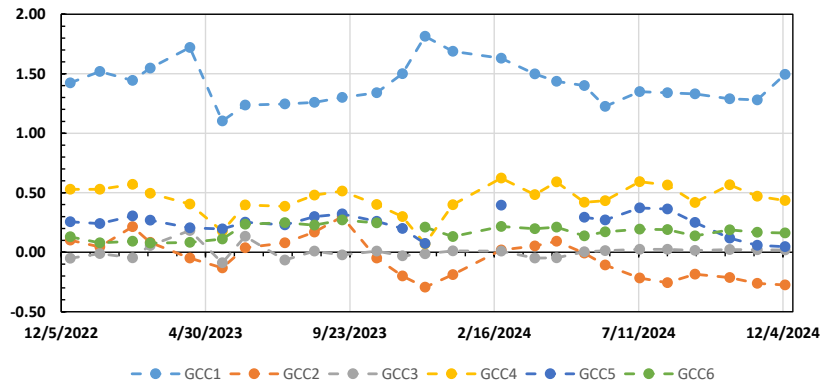


Vertical Gradients - Exterior SZ-IZ

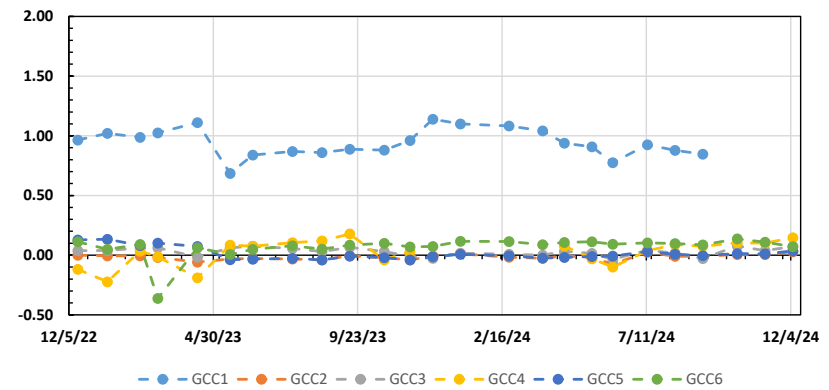

Vertical Gradients - Interior IZ-DZ

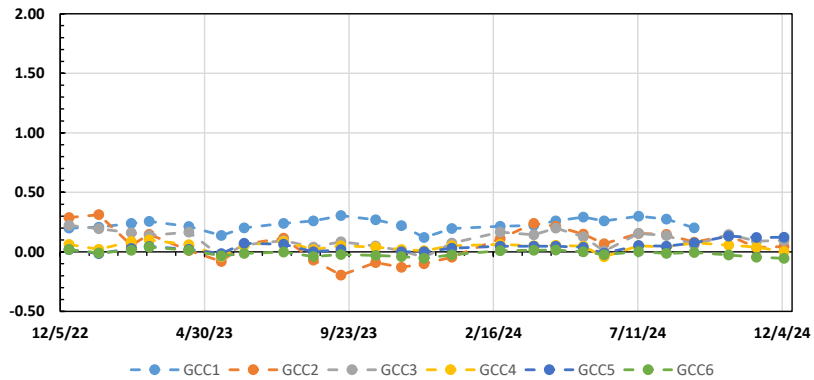

Vertical Gradients - Exterior IZ-DZ

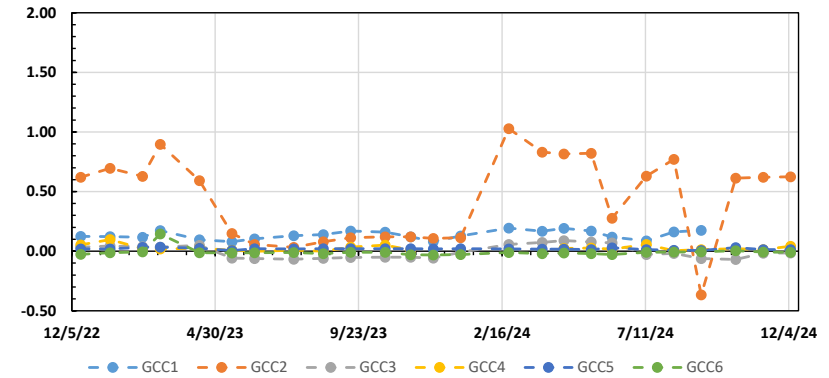



ATTACHMENT B-3

WATER LEVELS AND HORIZONTAL
GRADIENTS TABLE

Attachment B-3

Water Levels and Horizontal Gradients Table Arkema Inc. Facility Portland, Oregon

Gradient Cluster	Well Pair Zone	Exterior Well	Water Elevation (ft NAVD88)	Interior Well	Water Elevation (ft NAVD88)	Horizontal Gradient (ft/ft)
GCC1	Shallow	PA-03	26.76	PA-04	27.32	-0.006
	Intermediate	PA-17iR	11.33	PA-10i	12.52	-0.011
	Deep	PA-27d	10.79	PA-18d	10.48	0.003
GCC2	Shallow	MWA-2	9.40	PA-05	6.79	0.038
	Intermediate	MWA-8i	8.96	PA-11i	9.73	-0.011
	Deep	PA-19d	7.99	PA-30d	9.41	-0.026
GCC3	Shallow	MWA-69	9.80	PA-06	11.65	-0.017
	Intermediate	MWA-66i	8.81	PA-12i	11.46	-0.023
	Deep	PA-21d	9.01	PA-20d	9.59	-0.005
GCC4	Shallow	MWA-19	10.20	PA-28	13.37	-0.031
	Intermediate	MWA-34iR	9.16	PA-13i	10.59	-0.016
	Deep	MWA-58d	8.23	PA-22d	10.55	-0.026
GCC5	Shallow	MWA-47	9.33	PA-07	13.27	-0.038
	Intermediate	PA-29i	8.98	PA-14i	12.83	-0.071
	Deep	PA-24d	8.45	PA-23d	8.11	0.006
GCC6	Shallow	PA-09	11.21	PA-08	12.11	-0.016
	Intermediate	PA-16i	10.29	PA-15i	10.09	0.004
	Deep	PA-26d	10.62	PA-25d	12.12	-0.024

Positive horizontal gradient indicates an inward hydraulic gradient across the GWBW.

Horizontal gradient calculated as (Exterior Elevation – Interior Elevation) / Horizontal distance.

* = anomalous groundwater elevation

** = horizontal gradient cannot be calculated due to anomalous elevation reading

ft NAVD88 = feet North American Vertical Datum of 1988

^M = manual groundwater elevation measurement



ATTACHMENT B-4

WATER LEVELS AND VERTICAL
GRADIENTS TABLE

Attachment B-4

Water Levels and Vertical Gradients Table Arkema Inc. Facility Portland, Oregon

Region	Pair	Gradient Cluster	Upper Well	Water Elevation (ft NAVD88)	Lower Well	Water Elevation (ft NAVD88)	Vertical Gradient (ft/ft)
Interior	SZ-IZ	GCC1	PA-04	27.32	PA-10i	12.52	1.49
		GCC2	PA-05	6.79	PA-11i	9.73	-0.28
		GCC3	PA-06	11.65	PA-12i	11.46	0.02
		GCC4	PA-28	13.37	PA-13i	10.59	0.44
		GCC5	PA-07	13.27	PA-14i	12.83	0.05
		GCC6	PA-08	12.11	PA-15i	10.09	0.16
	IZ-DZ	GCC1	PA-10i	12.52	PA-18d	10.48	0.27
		GCC2	PA-11i	9.73	PA-30d	9.41	0.05
		GCC3	PA-12i	11.46	PA-20d	9.59	0.10
		GCC4	PA-13i	10.59	PA-22d	10.55	0.00
		GCC5	PA-14i	12.83	PA-23d	8.11	0.12
		GCC6	PA-15i	10.09	PA-25d	12.12	-0.05
Exterior	SZ-IZ	GCC1	PA-03	26.76	PA-17iR ^M	11.33	0.98
		GCC2	MWA-2	9.40	MWA-8i	8.96	0.03
		GCC3	MWA-69	9.80	MWA-66i	8.81	0.07
		GCC4	MWA-19	10.20	MWA-34iR	9.16	0.15
		GCC5	MWA-47	9.33	PA-29i	8.98	0.04
		GCC6	PA-09	11.21	PA-16i	10.29	0.07
	IZ-DZ	GCC1	PA-17iR ^M	11.33	PA-27d	10.79	0.08
		GCC2	MWA-8i	8.96	PA-19d	7.99	0.62
		GCC3	MWA-66i	8.81	PA-21d	9.01	-0.02
		GCC4	MWA-34iR	9.16	MWA-58d	8.23	0.04
		GCC5	PA-29i	8.98	PA-24d	8.45	0.01
		GCC6	PA-16i	10.29	PA-26d	10.62	-0.01

Positive vertical gradient indicates an downward hydraulic gradient.

Vertical gradient calculated as (Upper Elevation – Lower Elevation) / Screen Midpoint distance.

* = anomalous groundwater elevation

** = vertical gradient cannot be calculated due to anomalous elevation reading

DZ = Deep Zone

ft NAVD88 = feet North American Vertical Datum of 1988

IZ = Intermediate Zone

^M = manual groundwater elevation measurement

SZ = Shallow Zone



ATTACHMENT C

PROJECT SCHEDULE

ID	Task Name	Duration	Start	Finish	Timeline																											
1	Quarterly GW Monitoring																															
2	4th Quarter 2023 Groundwater Monitoring	70 days	Mon 12/11/23	Fri 3/15/24																												
7	1st Quarter 2024 Groundwater Monitoring	4 days	Mon 2/26/24	Thu 2/29/24																												
8	Sample Wells	4 days	Mon 2/26/24	Thu 2/29/24																												
9	Obtain Analytical Data	1 day	Mon 4/1/24	Mon 4/1/24																												
10	Data Validation	1 day	Mon 4/15/24	Mon 4/15/24																												
11	Report Completed	1 day	Fri 6/7/24	Fri 6/7/24																												
12	2nd Quarter 2024 Groundwater Monitoring	75 days	Mon 6/10/24	Fri 9/20/24																												
13	Sample Wells	5 days	Mon 6/10/24	Fri 6/14/24																												
14	Obtain Analytical Data	1 day	Thu 6/27/24	Thu 6/27/24																												
15	Data Validation	1 day	Tue 7/30/24	Tue 7/30/24																												
16	Report Completed	1 day	Fri 9/20/24	Fri 9/20/24																												
17	3rd Quarter 2024 Groundwater Monitoring	75 days	Thu 8/22/24	Wed 12/4/24																												
18	Sample Wells	5 days	Mon 9/9/24	Fri 9/13/24																												
19	Obtain Analytical Data	1 day	Wed 10/2/24	Wed 10/2/24																												
20	Data Validation	1 day	Fri 11/1/24	Fri 11/1/24																												
21	Report Completed	1 day	Wed 12/18/24	Wed 12/18/24																												
22	4th Quarter 2024 Groundwater Monitoring *	242 days	Fri 1/10/25	Fri 12/12/25																												
23	Sample Wells	5 days	Mon 12/8/25	Fri 12/12/25																												
24	Obtain Analytical Data	1 day	Fri 1/10/25	Fri 1/10/25																												
25	Data Validation	1 day	Tue 1/21/25	Tue 1/21/25																												
26	Report Completed	1 day	Mon 3/17/25	Mon 3/17/25																												
27	Monthly Progress Reports	264 days	Thu 2/15/24	Sat 2/15/25																												
28	December 2023 MPR	1 day	Thu 2/15/24	Thu 2/15/24																												
29	January 2024 MPR	1 day	Fri 3/15/24	Fri 3/15/24																												
30	February 2024 MPR	1 day	Mon 4/15/24	Mon 4/15/24																												
31	March 2024 MPR	1 day	Wed 5/15/24	Wed 5/15/24																												
32	April 2024 MPR	1 day	Mon 6/17/24	Mon 6/17/24																												
33	May 2024 MPR	1 day	Mon 7/15/24	Mon 7/15/24																												
34	June 2024 MPR	1 day	Thu 8/15/24	Thu 8/15/24																												
35	July 2024 MPR	1 day	Mon 9/16/24	Mon 9/16/24																												
36	August 2024 MPR	1 day	Tue 10/15/24	Tue 10/15/24																												
37	September 2024 MPR	1 day	Fri 11/15/24	Fri 11/15/24																												
38	October 2024 MPR	1 day	Mon 12/16/24	Mon 12/16/24																												
39	November 2024 MPR	1 day	Wed 1/15/25	Wed 1/15/25																												
40	December 2024 MPR	1 day	Sat 2/15/25	Sat 2/15/25																												
41	Datagaps Workplan	175 days	Mon 4/1/24	Fri 11/29/24																												
42	Data Gaps Investigations	87 days	Mon 12/2/24	Mon 3/31/25																												
43	IRAM 1- Acid Plant Area Soil & GW ISS *	700 days	Mon 4/1/24	Thu 12/3/26																												
44	PDI Workplan Submittal	35 days	Mon 4/1/24	Fri 5/17/24																												
45	ODEQ Review	10 days	Thu 5/23/24	Wed 6/5/24																												
46	PDI Workplan Revisions	23 days	Wed 6/5/24	Fri 7/5/24																												
47	PDI Field Effort - Site Prep	15 days	Mon 6/17/24	Fri 7/5/24																												
48	PDI Field Effort - Phase I	40 days	Mon 7/8/24	Fri 8/30/24																												
49	Treatability Study Testing	122 days	Mon 9/2/24	Mon 2/17/25																												
50	PDI Field Effort - Phase II	24 days	Mon 9/30/24	Thu 10/31/24																												
51	PDI Report	70 days	Mon 9/2/24	Fri 12/6/24																												
52	Pre-final Design Report	80 days	Wed 12/11/24	Mon 3/31/25																												
53	ODEQ Review	20 days	Tue 4/1/25	Mon 4/28/25																												
54	Final Design Report	21 days	Tue 4/29/25	Tue 5/27/25																												
55	IRAM 1 Implementation (Summer/Fall 2025)	67 days	Mon 9/1/25	Tue 12/2/25																												
56	IRAM 1 Performance Monitoring	262 days	Wed 12/3/25	Thu 12/3/26																												
57	IRAM 2-Enhanced ISCR Perchlorate & CrVI In Chlorate Plant Area, if needed (Summer 2026 implementation)	261 days	Mon 9/15/25	Mon 9/14/26																												
58	IRAM 3-Remove Human Health Direct Contact Hot Spots, if needed (Summer 2028 implementation)	261 days	Mon 9/13/27	Mon 9/11/28																												
59	IRAM 4-Enhanced ISCR of Acid Plant Vicinity, if needed (Summer 2027 implementation)	207 days	Fri 12/4/26	Mon 9/20/27																												
Arkema Portland Monthly Progress Report Attachment C					Legend																											
Task					Summary																											
Split					Project Summary																											
Milestone					Inactive Task																											
Inactive Milestone					Inactive Summary																											
Manual Task					Manual Summary																											
Duration-only					Manual Summary Rollup																											
Start-only					Finish-only																											
External Milestone					External Tasks																											
Manual Progress					Progress																											
Deadline																																



ATTACHMENT D

AVERAGE GROUNDWATER
EXTRACTION RATE GRAPH

Attachment D

Average Groundwater Extraction Rate Graph
Arkema Inc. Facility
Portland, Oregon

